

Highlights

Repair

Needs	Capacity	Completed	Ongoing	Gap
7,358	5,921	5,707 (78%)	0 (0%)	1,651 (22%)

District	Needs	Completed	Ongoing	Gap	Progress (Completed Ongoing Gap)	
Spira	3,674	2,610	0	1,064	71%	29%
Gayan	1,806	1,806	0	0	100%	
Barmal	965	965	0	0	100%	
Dwamande Shamal	147	147	0	0	100%	
Tani	478	105	0	373	22%	78%
Ziruk	288	74	0	214	26%	74%


Rebuild

Needs	Capacity	Completed	Ongoing	Gap
8,027	6,465	5,597 (70%)	868 (11%)	1,562 (19%)

District	Needs	Completed	Ongoing	Gap	Progress (Completed Ongoing Gap)	
Spira	2,441	1,717	0	724	70%	30%
Barmal	1,475	1,407	68	0	95%	5%
Gayan	3,752	2,408	800	544	64%	21% 14%
Dwamande Shamal	40	38	0	2	95%	5%
Tani	27	27	0	0	100%	
Ziruk	292	0	0	292	100%	



Earthquake in southeastern region - June 2022

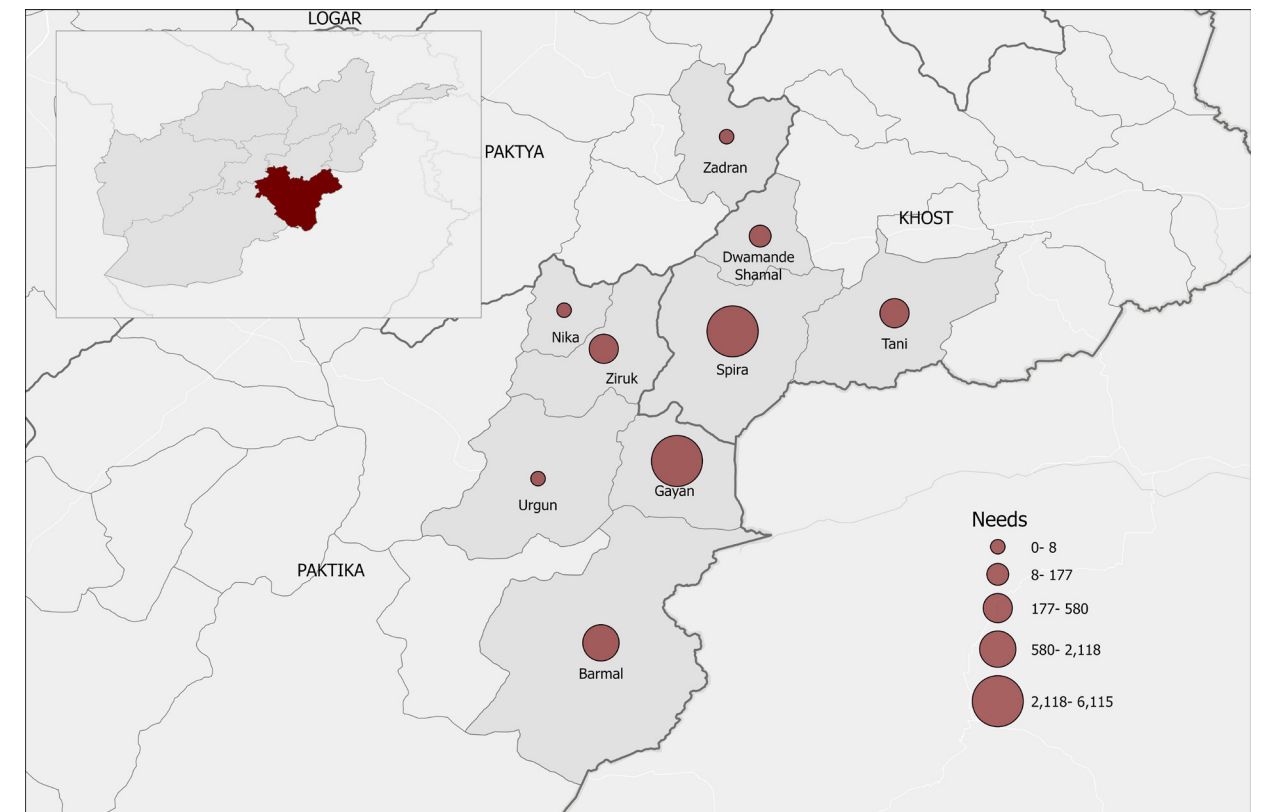

Southeastern Region affected districts

Partners Progress

Repair

Capacity	Completed	Ongoing	Committed
5,921	5,707 (96%)	0 (0%)	214 (4%)

Organizations	Capacity	Completed	Ongoing	Committed	Progress (Completed Ongoing Committed)
IFRC/ARCS	2,083	2,083	0	0	100%
IOM	1,725	1,725	0	0	100%
Johanniter	500	500	0	0	100%
NAC	479	479	0	0	100%
Actionaid	435	435	0	0	100%
OHW	150	150	0	0	100%
IRC	130	130	0	0	100%
NRC	101	101	0	0	100%
CARE/UNDP	48	48	0	0	100%
AABRAR	31	31	0	0	100%
Cordaid	20	20	0	0	100%
ORD	5	5	0	0	100%
WSTA	214	0	0	214	100%

Rebuild

Capacity	Completed	Ongoing	Committed
6,465	5,597 (87%)	0 (0%)	868 (13%)

Organizations	Capacity	Completed	Ongoing	Committed	Progress (Completed Ongoing Committed)
UNHCR	2,300	1,500	0	800	65% 35%
Cordaid	689	689	0	0	100%
ORD	432	432	0	0	100%
IOM	1,513	1513	0	0	100%
AABRAR	234	234	0	0	100%
NAC	184	184	0	0	100%
IRW	147	147	0	0	100%
Actionaid	143	143	0	0	100%
NRC	143	143	0	0	100%
CWW	105	105	0	0	100%
IRC	100	100	0	0	100%
WSTA	68	0	0	68	0%
CWSA	50	50	0	0	100%
UNDP (SCA)	44	44	0	0	100%
UNDP (CARE)	8	8	0	0	100%
IFRC/ARCS	305	305	0	0	100%
